

April 25, 2024

LeftField

DRA

MEETING MINUTES



SUGGESTED VOTE:

Vote to approve meeting minutes from the March 20, 2024 SBC Meeting.



DRA AMENDMENT #4

SOUTH SHORE

SOUTH

Total: \$27,797.00

Fee for Basic Services	Original Contract	Previous Amendments	Amount of This Amendment	Total of All Amendments	
Feasibility Study/ Schematic Design Phase	\$1,000,000	\$ 66,385.00	\$ 27,797.00	\$ 1,094,182.00	
Total Fee	\$1,000,000.00	\$ 66,385.00	\$ 27,797.00	\$ 1,094,182.00	

AMENDMENT SCOPE:

Hazmat Sampling, Analysis & Estimate:

Fee: \$25,270.00

10% DRA Markup: \$2,527.00

Total Amendment #4: \$27,797.00

SCHEDULE FOR WORK:

- Samples collected over April Vacation
- Estimate to be prepared to include in SD

Project Estimate Set

INVOICES

Total: \$84,000.00



INVOICES								
ProPay Code	Invoice Date	Vendor	Invoice #	Budget Category	Description of Services	Invoice \$		
0001-0000	3/31/24	LeftField	12	OPM – Feasibility Study/ Schematic Design	OPINI Feasibility Study Services	\$29,000.00		
0002-0000	3/31/24	DRA	7	A/E - Feasibility Study/ Schematic Design	A/E Feasibility Study Services March 1 – March 31, 2024	\$55,000.00		
					TOTAL:	\$84,000.00		

BUDGET UPDATE



South Shore Regional Vocational Technical High School - Hanover, MA							April 30, 2024			
Total Project I	Budget Status Report									
ProPay Code	Description	Total Project Budget	Authorized Changes	Revised Total Budget	Total Committed	% Cmtd to Date	Actual Spent to Date	% Spent to Date	Balance To Spend	Comments
	FEASIBILITY STUDY AGREEMENT									
0001-0000	OPM Feasibility Study/Schematic Design	\$ 400,000	\$28,050	\$ 428,050	\$ 428,050	100%	\$ 323,900	76%	\$ 104,150	
0002-0000	A&E Feasibility Study/Schematic Design	\$ 1,100,000)	\$ 1,100,000	\$ 1,094,182	99%	\$ 594,446	54%	\$ 505,554	
0003-0000	Environmental & Site	\$ 300,000)	\$ 300,000	\$ -	0%	\$ -	0%	\$ 300,000	
0004-0000	Other	\$ 200,000	\$ (28,050)	\$ 171,950	\$ -	0%	\$ -	0%	\$ 171,950	
	SUB-TOTAL	\$ 2,000,000	-	\$ 2,000,000	\$ 1,522,232	76%	\$ 918,346	46%	\$ 1,081,654	
Г	TOTAL PROJECT BUDGET	\$ 2,000,000	\$ -	\$ 2,000,000	\$ 1,522,232	76%	\$ 918,346	46%	\$ 1,081,654	
_										
	FUNDING SOURCES	Max w/ Conting.	Max w/o Conting.							
	Maximum State Share	\$ 1,112,600	\$ 1,112,600	Project	Scope Items Excluded	Contingencies	Basis of Total	Reimbursement		
	Local Share	\$ 887,400	\$ 887,400	Budget	scope items excluded	contingencies	Facilities Grant	Rate		
	SUB-TOTAL	\$ 2,000,000	\$ 2,000,000	\$ 2,000,000	\$ -	\$ -	\$ 2,000,000	55.63%		

 All Contract Amendments have been committed against the original budget to indicate the remaining funds in each Budget Category

Committed:76%

Expended: 46%

Anticipated Extra Services/

Reimbursables:

Uncommitted Funds:

\$200,000

\$477,768

 All Invoices have been indicated in the Budget

Remaining Funds:

\$277,768

MSBA UPDATE



The MSBA Approved the South Shore Tech project to proceed into the Schematic Design phase at their April 24, 2024 Board of Directors Meeting

- Next Steps:
 - Submit Schematic Design Budget to MSBA by mid-August
 - Submit Schematic Design Report to MSBA by August 29, 2024

LeftField has met with MSBA and determined that the District's reimbursement rate is weighted based on the sending communities' enrollment numbers

CM AT-RISK UPDATE



CM at-RISK PROCUREMENT

- 3/27/24 Statement of Qualifications (SOQs) Due
- 4/04/24 Selection Committee Met to Review SOQs
- 4/08/24 Request for Proposals (RFP) sent to qualified CMs
- 5/1/24 Technical and Price Proposals Due
- 5/9 5/10 Selection Committee Interviews CMs
- 5/10/24 Selection Committee Deliberations
- 5/10/24 Notice of Award
- TBD SBC Approves CM Contract

AVAILABLE FEASIBILITY FUNDS

- Uncommitted Funds Sufficient
- \$ 277,768 Feasibility Study Contingency
- Expected CMR Feasibility Pre-Con Fee range: \$55,000 to \$65,000

All Prequalification/Selection Committee

Meetings, including CM Interviews,

are public meetings.



- 1. Programming Interviews
- 2. Schematic Design Update
- 3. Sustainability



Programming Update – Instructor interviews

SOUTH SHORE Technical High School





SOUTH SHORE Technical High School




First Floor Plan





SOUTH SHORE

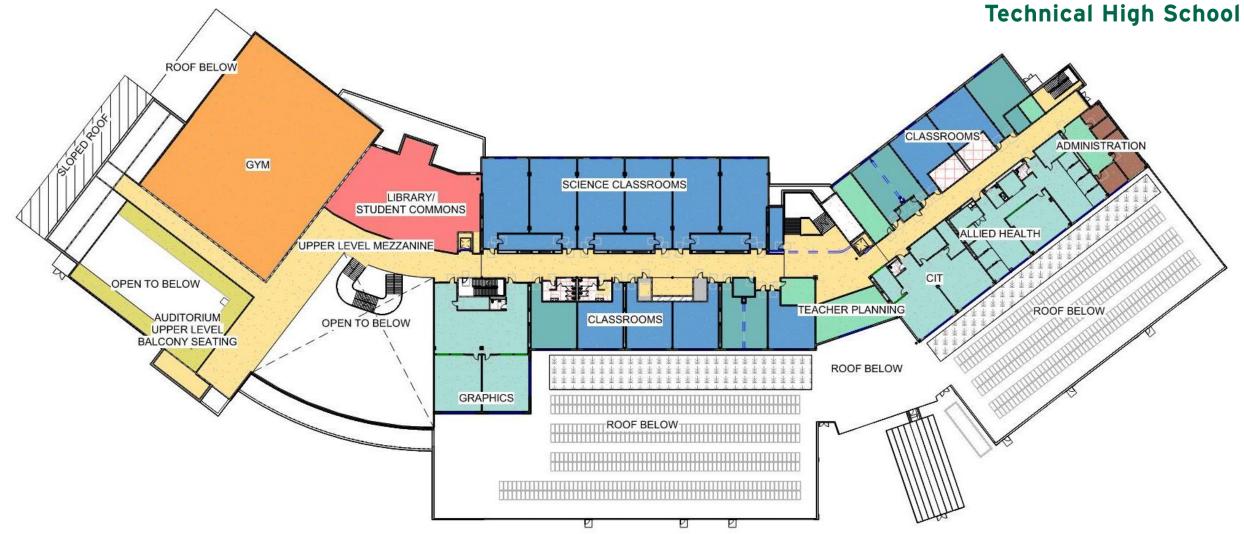






SOUTH SHORE

Technical High School

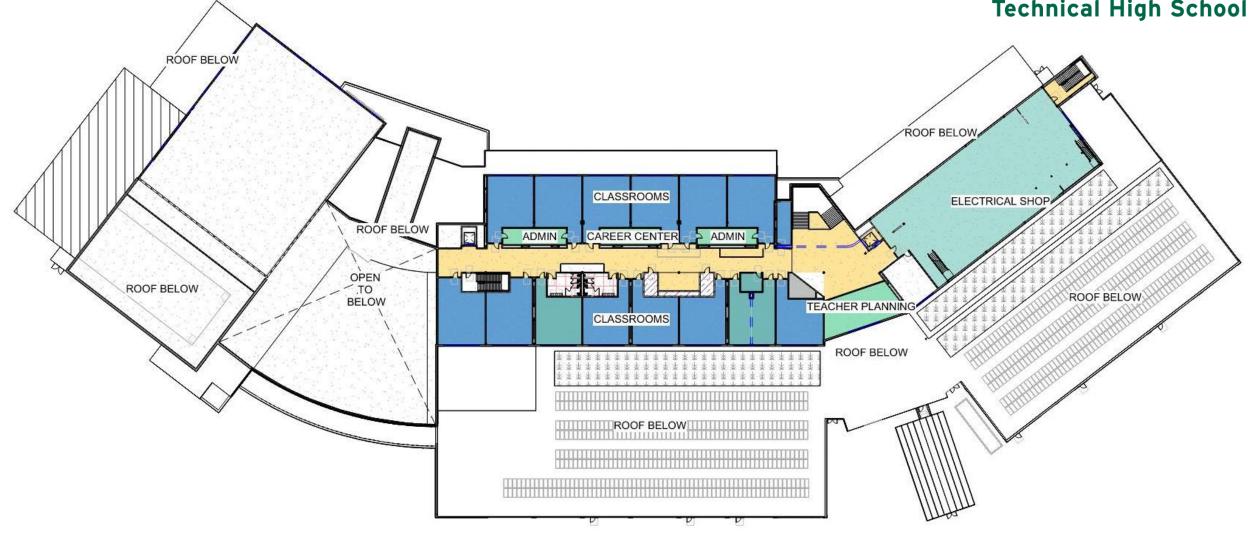







Sustainability

SOUTH SHORE

Technical High School

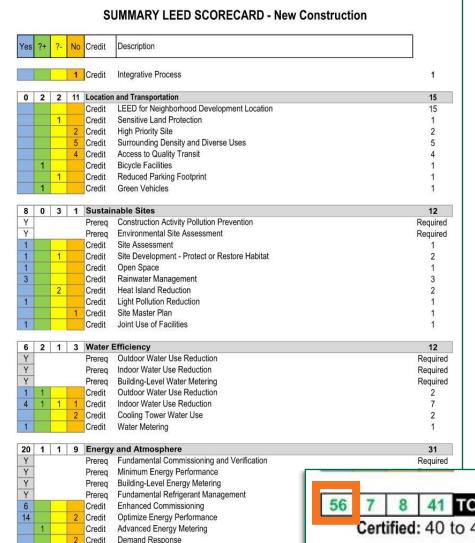

Renewable Energy Production Enhanced Refrigerant Management

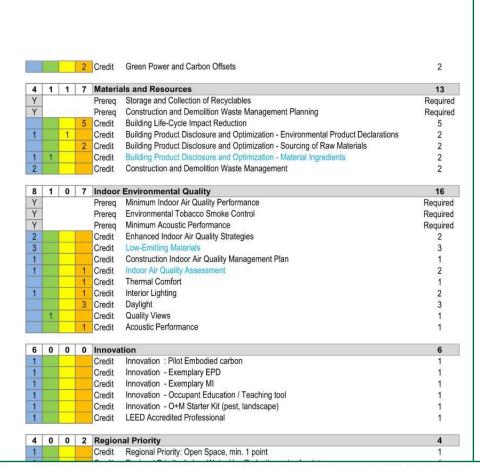

MSBA Incentive:

4 Additional reimbursement points

41 TOTALS

Possible Points:

110

Certified: 40 to 49 points, Silver: 50 to 59 points, Gold: 60 to 79 points, Platinum: 80 to 110



